




Lincoln Street Improvements, 84th Street to Fort Street Paving and Storm Sewer



Task Name	Duration	Start	Finish
Lincoln Street, 84th Street to Fort Street	13 days	Mon 3/6/17	Mon 3/20/17
Pre Phase Work	13 days	Mon 3/6/17	Mon 3/20/17
OPPD - Relocate Power Poles	13 days	Mon 3/6/17	Mon 3/20/17
CenturyLink- Relocate Fiber Optic (Concurrent if Required)	13 days	Mon 3/6/17	Mon 3/20/17
Tree Removals (Box Culvert & Sta. 37+00 - 42+00 Lt.)	2 days	Mon 3/6/17	Tue 3/7/17
Pavement Removals (Lamb of God Parking Lot)	1 day	Wed 3/8/17	Wed 3/8/17
Site Grading (Construct Surcharge Cheyenne Roundabout)	10 days	Thu 3/9/17	Mon 3/20/17
Install Tempoary Pipe & Riprap at Surcharge	2 days	Sun 3/19/17	Mon 3/20/17
Phase 1 Sta. 40+00 - 46+00	22 days	Mon 3/20/17	Mon 4/10/17
OPPD - Relocate Power Poles	22 days	Mon 3/20/17	Mon 4/10/17
CenturyLink- Relocate Fiber Optic (Concurrent if Required)	22 days	Mon 3/20/17	Mon 4/10/17
Black Hills Energy - Relocate Natural Gas (Concurrent if Required)	22 days	Mon 3/20/17	Mon 4/10/17
Install Site BMP's	1 day	Mon 3/20/17	Mon 3/20/17
Clearing and Grubbing	1 day	Mon 3/20/17	Mon 3/20/17
Pavement Removals	3 days	Mon 3/20/17	Wed 3/22/17
Contractor Site Utilities (Storm & Sanitary, Sta. 40+00 - 43+00)	5 days	Thu 3/23/17	Mon 3/27/17
Site Grading (Jackson St. Intersection)	2 days	Thu 3/23/17	Fri 3/24/17
Street Paving (Jackson St. Intersection)	12 days	Sat 3/25/17	Wed 4/5/17
Backfill & Shoulder (Jackson St. Intersection)	1 day	Thu 4/6/17	Thu 4/6/17
Sidewalks (Jackson St.)	4 days	Fri 4/7/17	Mon 4/10/17
Phase 2A Sta. 46+00 - 51+22	28 days	Mon 4/10/17	Sun 5/7/17
OPPD - Relocate Power Poles	28 days	Mon 4/10/17	Sun 5/7/17
CenturyLink- Relocate Fiber Optic (Concurrent if Required)	28 days	Mon 4/10/17	Sun 5/7/17
Black Hills Energy - Relocate Natural Gas (Concurrent if Required)	28 days	Mon 4/10/17	Sun 5/7/17
Install Site BMP's	1 day	Mon 4/10/17	Mon 4/10/17
Clearing and Grubbing	1 day	Mon 4/10/17	Mon 4/10/17
Pavement Removals	2 days	Mon 4/10/17	Tue 4/11/17
Site Grading	2 days	Wed 4/12/17	Thu 4/13/17
Street Paving	16 days	Fri 4/14/17	Sat 4/29/17
Backfill & Shoulder	2 days	Sun 4/30/17	Mon 5/1/17
Sidewalks	4 days	Tue 5/2/17	Fri 5/5/17
Site Restoration/ Temp. Striping	2 days	Sat 5/6/17	Sun 5/7/17
Phase 2B Sta. 34+00 - 45+00	57 days	Sun 5/7/17	Sun 7/2/17
CenturyLink- Relocate Fiber Optic (Concurrent if Required)	57 days	Sun 5/7/17	Sun 7/2/17
Black Hills Energy - Relocate Natural Gas (Concurrent if Required)	57 days	Sun 5/7/17	Sun 7/2/17
Install Site BMP's	1 day	Sun 5/7/17	Sun 5/7/17
Clearing and Grubbing	1 day	Sun 5/7/17	Sun 5/7/17
Pavement Removals	2 days	Sun 5/7/17	Mon 5/8/17
Contractor Site Utilities (Storm, Sanitary & Water)	21 days	Tue 5/9/17	Mon 5/29/17
Construct Modified Impact Stilling Basin	28 days	Sat 5/20/17	Fri 6/16/17
Site Grading	3 days	Tue 5/30/17	Thu 6/1/17
Street Paving	20 days	Fri 6/2/17	Wed 6/21/17
Backfill & Shoulder	2 days	Thu 6/22/17	Fri 6/23/17
Inlets & Sidewalks	7 days	Sat 6/24/17	Fri 6/30/17
Site Restoration/Temp. Striping	2 days	Sat 7/1/17	Sun 7/2/17
Phase 2C Sta. 20+00 - 22+00 (Box Culvert)	49 days	Mon 5/15/17	Sun 7/2/17
Install Site BMP's	1 day	Mon 5/15/17	Mon 5/15/17
Clearing and Grubbing	1 day	Tue 5/16/17	Tue 5/16/17
Pavement Removals	1 day	Tue 5/16/17	Tue 5/16/17
Construct Reinforced Box Culvert	47 days	Wed 5/17/17	Sun 7/2/17
Phase 3A Sta. 20+00 - 27+00	28 days	Mon 6/5/17	Sun 7/2/17
Install Site BMP's	1 day	Mon 6/5/17	Mon 6/5/17
Clearing and Grubbing	1 day	Mon 6/5/17	Mon 6/5/17
Pavement Removals	2 days	Tue 6/6/17	Wed 6/7/17

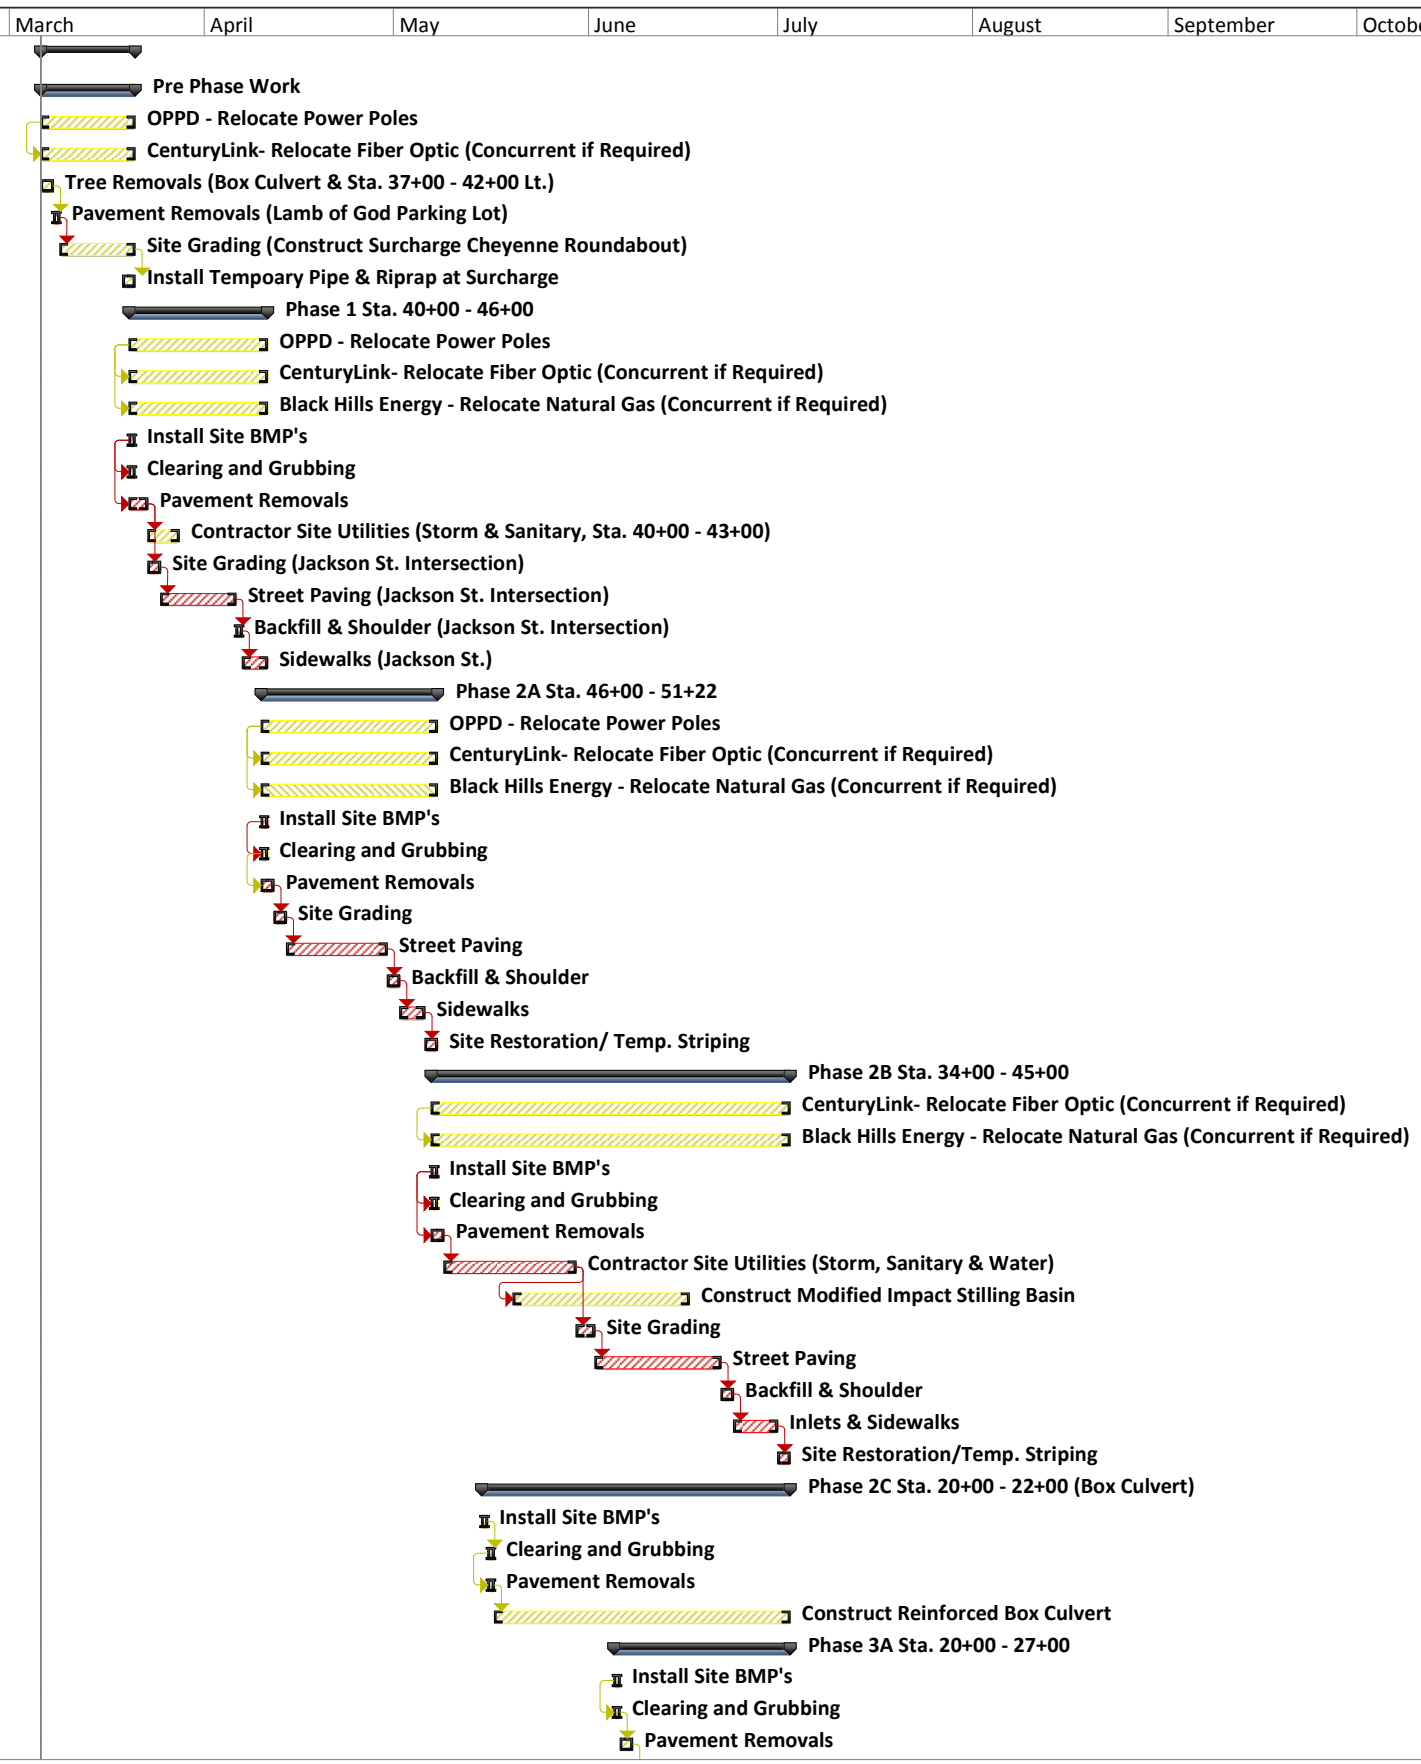

Vrana Proposed Schedule



Lincoln Street Improvements, 84th Street to Fort Street Paving and Storm Sewer



Task Name	Duration	Start	Finish	February	March	April	May	June	July	August	September	October	November	December	January
Contractor Site Utilities (Storm & Water)	25 days	Thu 6/8/17	Sun 7/2/17												
Phase 3B Sta. 2+00 - 34+00	107 days	Mon 7/3/17	Tue 10/17/17												
CenturyLink- Relocate Fiber Optic (Concurrent if Required)	40 days	Mon 7/3/17	Fri 8/11/17												
Black Hills Energy - Relocate Natural Gas (Concurrent if Required)	40 days	Mon 7/3/17	Fri 8/11/17												
Install Site BMP's	3 days	Mon 7/3/17	Wed 7/5/17												
Clearing and Grubbing	4 days	Thu 7/6/17	Sun 7/9/17												
Pavement Removals (2+00 - 20+00 & 27+00 - 34+00)	4 days	Mon 7/10/17	Thu 7/13/17												
Contractor Site Utilities (Storm & Water)	21 days	Fri 7/14/17	Thu 8/3/17												
Construct Reinforced Box Wing Wall & Apron	28 days	Mon 7/3/17	Sun 7/30/17												
Site Grading	7 days	Fri 7/28/17	Thu 8/3/17												
Street Paving	60 days	Fri 8/4/17	Mon 10/2/17												
Backfill & Shoulder	5 days	Tue 10/3/17	Sat 10/7/17												
Inlets & Sidewalks	10 days	Sun 10/8/17	Tue 10/17/17												
Phase 3C Sta. 2+00 - 51+22	36 days	Tue 10/17/17	Tue 11/21/17												
Finish Grading	7 days	Sun 10/15/17	Sat 10/21/17												
Permanent Seeding/Sod	10 days	Sun 10/22/17	Tue 10/31/17												
Post Mounted Signs	10 days	Wed 11/1/17	Fri 11/10/17												
Permanent Striping	10 days	Sat 11/11/17	Mon 11/20/17												
Open Project to Traffic	1 day	Tue 11/21/17	Tue 11/21/17												

